

Envelope Sealing Performed For:

Indian River Heights, Taylor Clark 206 13th Ave Vero Beach, FL 32962		AEROBARRIER CASE ID: 8331 SEAL DESCRIPTION: Clark HARDWARE: AeroBarrier Connect TECHNICIAN: Samuel Hjalmeby
DATE: 10/31/2024	BUILDING TYPE: Single Family Detached	

Envelope Sealing Results:

BEFORE SERVICE

737.8 CFM of Leakage, equivalent to a
88.8 Square Inch Hole, or
4.53 Air Changes per Hour

(for your 1147-ft² structure enclosing a volume of 9770 cubic feet)


AFTER SERVICE

132.6 CFM of Leakage, equivalent to a
16.0 Square Inch Hole, or
0.81 Air Changes per Hour


This corresponds to a
82.0% Reduction in Envelope Leakage

NOTE: Envelope leakage and air-change results are calculated at a standard pressure of 50 Pa.
Sealing time elapsed: 2:44:53

Envelope Sealing Progress:

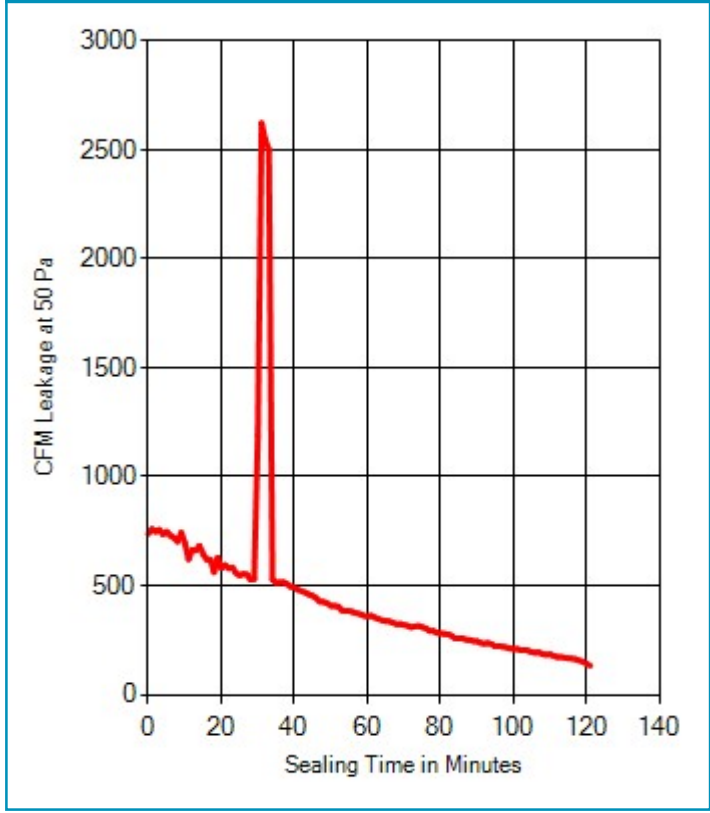

Envelope Sealing Performed By:

	HomeAirSeal, LLC 1525 Old Dixie Hwy Vero Beach, FL 32960 Phone: 772-774-4814
---	--

NOTES: a) A certified HVAC contractor or rater should be used to assess the need for enhanced/balanced mechanical equipment as the desired leakage is reduced. b) This certificate provides results based on an enclosure test, using positive pressure. A final blower door test may still be required.
